

Pharmacy to Kennedy Station Construction Liaison Committee Meeting

Eglinton Crosstown LRT

July 27, 2021

METROLINX LAND ACKNOWLEDGMENT

Let us take a moment to acknowledge that we are on the traditional territory of Indigenous Peoples including the Anishnabeg, the Haudenosaunee and the Wendat peoples.

We are all Treaty people. Many of us have come here as settlers and immigrants ... in this generation or generations past.

Metrolinx declares its commitment to building meaningful relationships with Indigenous Peoples.

We acknowledge the historic and continued impacts of colonization and the need to work towards meaningful reconciliation with the original caretakers of this land.

We acknowledge that Metrolinx operates on lands covered by 20 Treaties, and that we have a responsibility to recognize and value the rights of Indigenous Nations and Peoples and conduct business in a matter that is built on the foundation of trust, respect and collaboration.

Section Three and Four At-Grade: O'Connor Stop to Ionview Stop

CONSTRUCTION ACTIVITIES

Location	Activity	Approx. Date & Duration
Vehicle Testing	Brentcliffe - Kennedy	Ongoing through December 2021
Road Restoration	Brentcliffe - Kennedy	August 2021 - Fall 2021
Rosemount Drive	Closure for Massey Creek river lining landscaping works	July 5 - August 2, 2021
O'Connor Stop (Victoria Park Ave)	<ul style="list-style-type: none"> Shelter finishing activities; handrail installation Platform ramps & curbs; electrical finishes 	<ul style="list-style-type: none"> Largely completed June 2021 Ongoing through Summer 2021
Pharmacy Stop	<ul style="list-style-type: none"> Shelter finishing activities; handrail installation Platform ramps & curbs; electrical finishes 	<ul style="list-style-type: none"> Largely completed June 2021 Ongoing through Summer 2021
Hakimi Lebovic Stop	<ul style="list-style-type: none"> Shelter finishing activities; handrail installation Platform ramps & curbs; electrical finishes 	<ul style="list-style-type: none"> Largely completed June 2021 Ongoing through Summer 2021
Golden Mile Stop (Warden Ave)	<ul style="list-style-type: none"> Mock-Up of Green Track Shelter finishing activities; handrail installation Platform ramps & curbs; electrical finishes 	<ul style="list-style-type: none"> Completed July 2021 Largely completed June 2021 Ongoing through Summer 2021
Birchmount Stop	<ul style="list-style-type: none"> Shelter finishing activities; handrail installation Platform ramps & curbs; electrical finishes 	<ul style="list-style-type: none"> Largely completed June 2021 Ongoing through Summer 2021
Ionview Stop	<ul style="list-style-type: none"> Shelter finishing activities; handrail installation Platform ramps & curbs; electrical finishes 	<ul style="list-style-type: none"> Largely completed June 2021 Ongoing through Summer 2021

EAST TESTING & COMMISSIONING



- On May 25, 26, 27, 31 and June 1 and 2, 6 light rail vehicles (LRVs) were delivered to the east end of the alignment.
- Testing and commissioning activities will be conducted between Brentcliffe Road and Kennedy Road.
- The LRVs will run mainly on the surface along a track in the center of Eglinton Avenue.

FINAL ROAD RESTORATION

BRENTCLIFFE - KENNEDY

- Final Road Restoration works will begin in August 2021 and last through Fall 2021
- The approximate timeline for road restoration of the At-Grade is:
 - August 2 - August 8, 2021: Aga Khan - Wynford
 - August - October 2021: Swift - Ionview
 - Fall TBC: Ionview - Kennedy
 - Fall TBC : Leslie - Aga Khan
- More specific details regarding the dates and locations of road restoration works will be communicated to the public as they become available

ROSEMOUNT DRIVE CLOSURE

July 5 - August 2, 2021



- Rosemount Drive north of Eglinton Avenue East will be closed from Monday July 5, 2021 - Monday August 2, 2021. This closure is required to facilitate river lining works at Massey Creek.
- North-south through-traffic and turns on will be prohibited for the duration of the work.

CONSTRUCTION PROGRESS PHOTOS



Kennedy Station

KENNEDY STATION UPDATE

Location	Activity	Approx. Date & Duration
Vehicle Testing	Brentcliffe - Kennedy	Ongoing through December 2021
Road Restoration	Brentcliffe - Kennedy	August 2021 - Fall 2021
East Service Road	Watermain relocation	June 28 - September 25, 2021
Kennedy Station Main Entrance	<ul style="list-style-type: none"> • Glazing • Installation of sewer management system • Conduit installation, plumbing and sheet metal works, tiling, masonry works • Art wall installation • Elevator & escalator installation 	<ul style="list-style-type: none"> • Completed July 2021 • Ongoing through July 2021 • Ongoing through 2021 • Ongoing through July 2021 • Ongoing through Fall 2021
Kennedy Station Box	<ul style="list-style-type: none"> • Concrete works, rebar, and shoring • Floor tiling 	<ul style="list-style-type: none"> • Ongoing - final roof slab set for August 2021 • Ongoing through September 2021
Kennedy Station GO Entrance and Platform	<ul style="list-style-type: none"> • Structural steel at Entrance • Excavation & concrete works • Retaining wall construction 	<ul style="list-style-type: none"> • Completed July 2021 • Ongoing through July 2021 • Ongoing through July 2021
Kennedy Station - East of GO	<ul style="list-style-type: none"> • Concrete & masonry works • Platform construction • Track installation • Electrical and mechanical works 	<ul style="list-style-type: none"> • Ongoing through September 2021 • Ongoing through Fall 2021 • Ongoing through August 2021 • Ongoing through 2021

EAST TESTING & COMMISSIONING



- On May 25, 26, 27, 31 and June 1 and 2, 6 light rail vehicles (LRVs) were delivered to the east end of the alignment.
- Testing and commissioning activities will be conducted between Brentcliffe Road and Kennedy Road.
- The LRVs will run mainly on the surface along a track in the center of Eglinton Avenue.

WATERMAIN RELOCATION WORKS AT EAST SERVICE ROAD


June 28 - September 25, 2021

- Watermain, storm, and sanitary system relocation and installation is taking place at the east service road at Kennedy Station
- Work will take place between June 28 - September 25, 2021 during standard working hours
- Short term work zones will be erected daily, partially occupying a lane in the service road.
- All lanes will be fully restored each night.
- Full vehicle and driveway access will be maintained at all times



KENNEDY CURRENT TRAFFIC CONFIGURATION


July 2021 for approx. three months

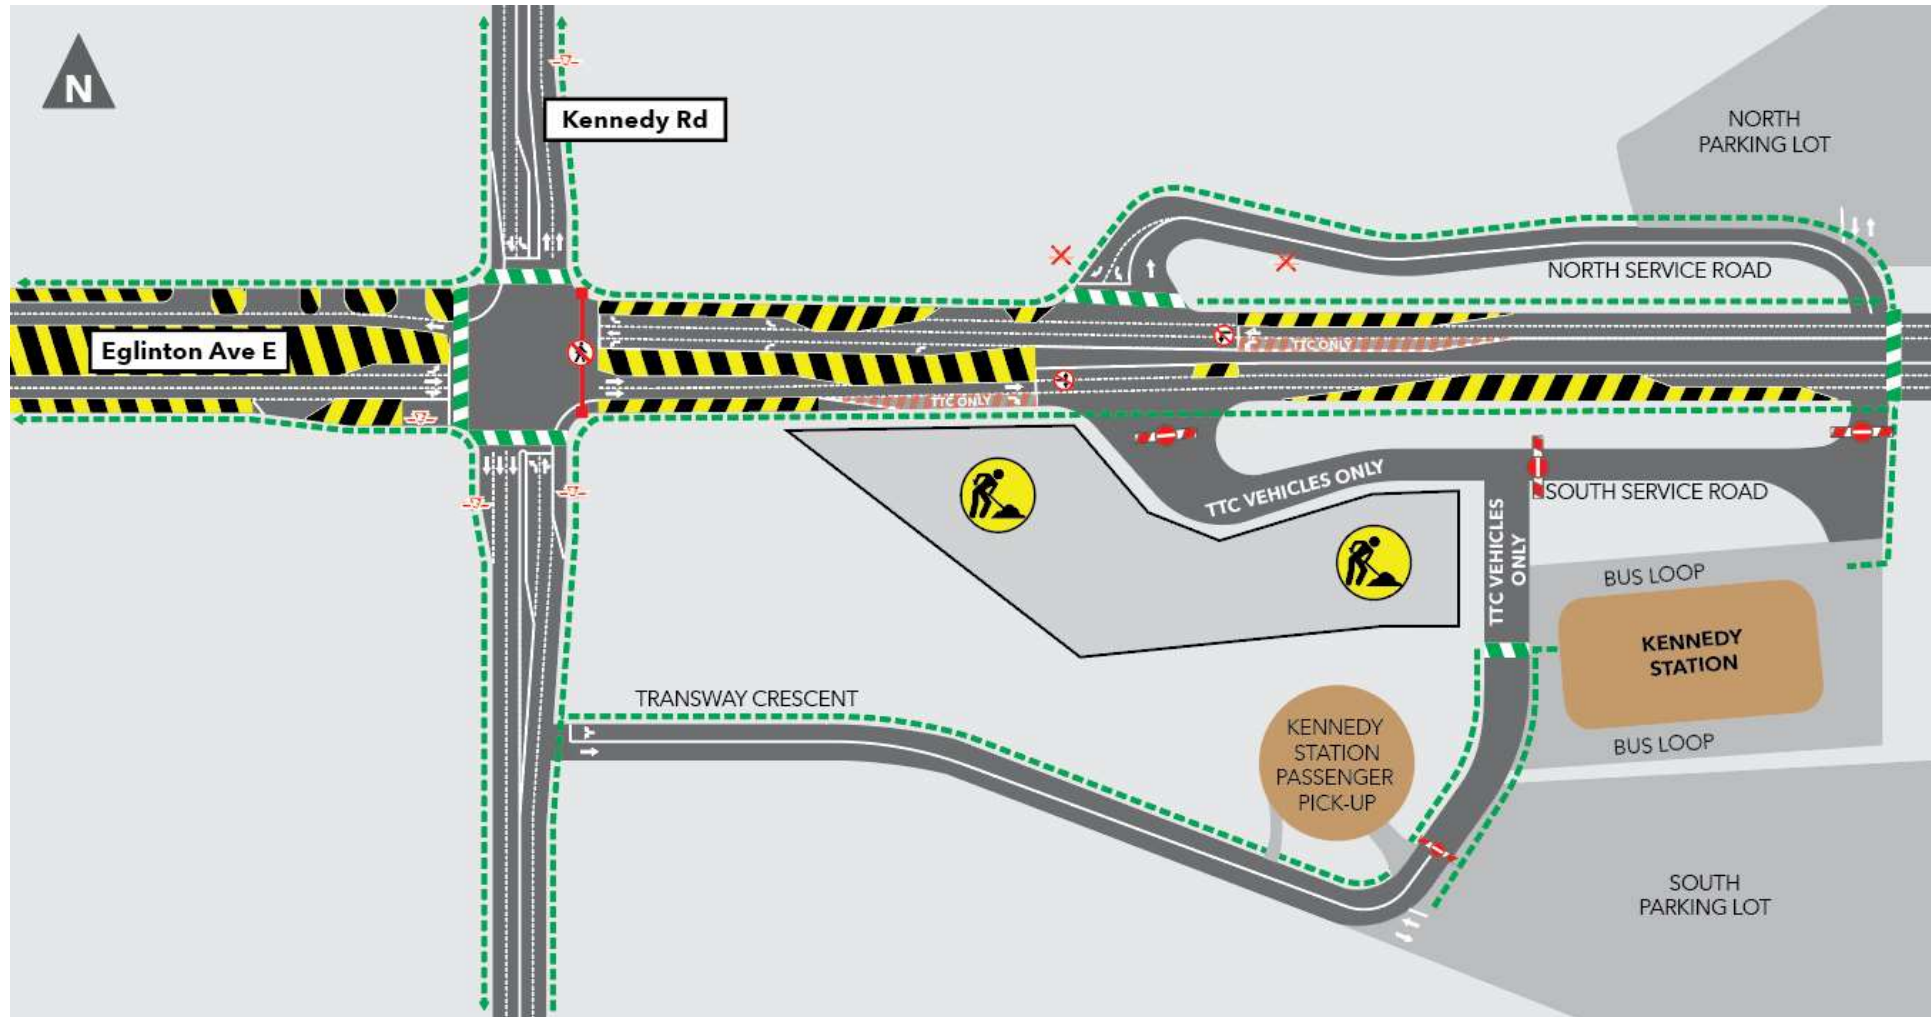

GO WEST PLATFORM RELOCATION AND PEDESTRIAN DETOUR

August 17, 2020 for approx. one year

- As part of GO Transit improvements at Kennedy GO Station, crews at Kennedy Station have temporarily relocated the west GO Transit platform
- Pedestrians will be rerouted through the Kennedy TTC Station
- This configuration will remain in place for approximately one year.

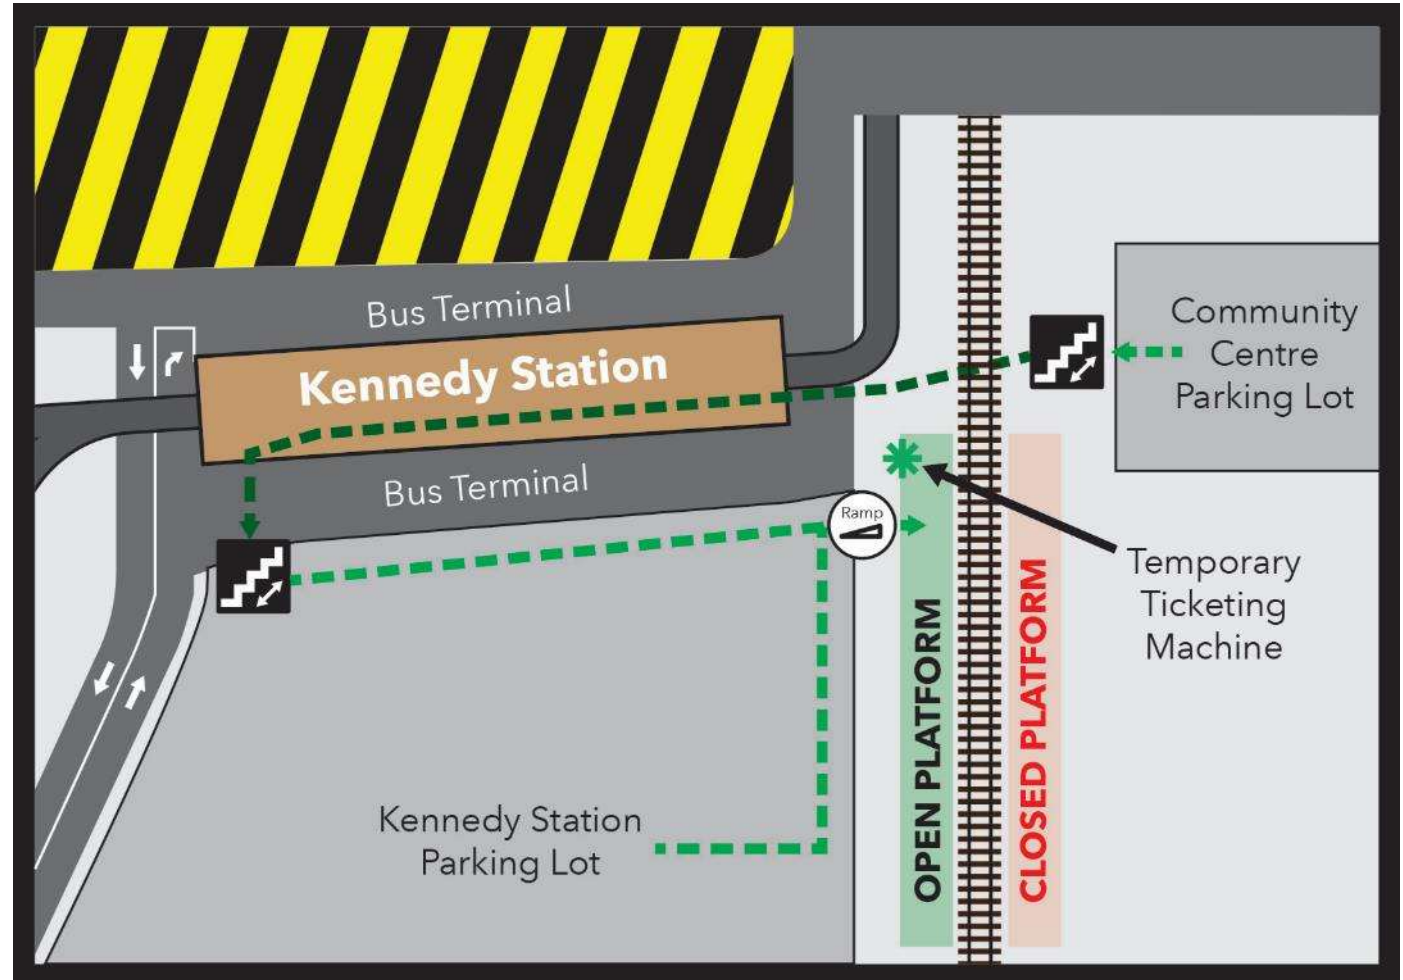

CONSTRUCTION PROGRESS PHOTOS



